Activity ID	Activity Name	Total Float	Original Duration	Start	Finish
The Big-PH01-Event02-IFC-After Fragnet		-158	735	11-Sep-25 A	15-Sep-27
Key Dates		-158	735	11-Sep-25 A	15-Sep-27
Milestone		-158	735	11-Sep-25 A	15-Sep-27
KD-MS-1000	Project Start Date		0	11-Sep-25 A	
KD-MS-1010	Contract Agreement		0	11-Sep-25 A	
KD-MS-1020	IFC Drawing Package		0	11-Sep-25 A	
KD-MS-1040	Ground Works Finish Date	-163	0		21-Oct-26*
KD-MS-1050	Project Finish Date	-158	0		15-Sep-27*
Event02-New IFC issued		-143	154	18-Mar-26	18-Aug-26
IFC Fragnet		-136	35	18-Mar-26	30-Apr-26
F-ENG-IFC-BL-SM	Revised IFC drawing package Issued	-136	0	18-Mar-26*	
F-ENG-IFC-DLY01	Duration of resubmission of the re-worked shop-drawings	-136	35	18-Mar-26	30-Apr-26
F-ENG-IFC-FM	Finishing of resubmission of the re-worked shop-drawings	-136	0		30-Apr-26
Affected-Activities-Submission		-116	78	02-May-26	06-Aug-26
B01		-131	39	02-May-26	20-Jun-26
Basement02		-113	21	02-May-26	25-May-26
F-SUB-B01-BAS02-1030	Submittal for Beams Conc. Dim. & RFT DWGs (B01) (Bas 02)	-132	18	02-May-26	21-May-26
F-SUB-B01-BAS02-1040	Submittal for Slabs Conc. Dim. & RFT DWGs (B01) (Bas 02)	-113	18	05-May-26	25-May-26
Basement01		-132	21	23-May-26	20-Jun-26
F-SUB-B01-BAS01-1030	Submittal for Beams Conc. Dim. & RFT DWGs (B01) (Bas 01)	-132	18	23-May-26	16-Jun-26
F-SUB-B01-BAS01-1040	Submittal for Slabs Conc. Dim. & RFT DWGs (B01) (Bas 01)	-132	18	26-May-26	20-Jun-26
B02		-93	39	02-May-26	20-Jun-26
Basement02		-107	21	02-May-26	25-May-26
F-SUB-B02-BAS02-1020	Submittal for Beams Conc. Dim.& RFT DWGs (B02) (Bas 02)	-107	18	02-May-26	21-May-26
F-SUB-B02-BAS02-1030	Submittal for Slabs Conc. Dim.& RFT DWGs (B02) (Bas 02)	-107	18	05-May-26	25-May-26
Basement01		-93	21	23-May-26	20-Jun-26
F-SUB-B02-BAS01-1020	Submittal for Beams Conc. Dim. & RFT DWGs (B02) (Bas 01)	-93	18	23-May-26	16-Jun-26
F-SUB-B02-BAS01-1030	Submittal for Slabs Conc. Dim. & RFT DWGs (B02) (Bas 01)	-93	18	26-May-26	20-Jun-26
B03		-116	36	21-Jun-26	03-Aug-26
Basement02		-132	21	21-Jun-26	15-Jul-26
F-SUB-B03-BAS02-1020	Submittal for Beams Conc. Dim. & RFT DWGs (B03) (Bas 02)	-132	18	21-Jun-26	12-Jul-26
F-SUB-B03-BAS02-1030	Submittal for Slabs Conc. Dim. & RFT DWGs (B03) (Bas 02)	-132	18	24-Jun-26	15-Jul-26
Basement01		-116	18	13-Jul-26	03-Aug-26
F-SUB-B03-BAS01-1020	Submittal for Beams Conc. Dim. & RFT DWGs (B03) (Bas 01)	-116	18	13-Jul-26	03-Aug-26
F-SUB-B03-BAS01-1030	Submittal for Slabs Conc. Dim. & RFT DWGs (B03) (Bas 01)	-113	10	16-Jul-26	28-Jul-26
B04		-116	39	21-Jun-26	06-Aug-26
Basement02		-124	21	21-Jun-26	15-Jul-26
F-SUB-B04-BAS02-1030	Submittal for Beams Conc. Dim. & RFT DWGs (B04) (Bas 02)	-124	18	21-Jun-26	12-Jul-26
F-SUB-B04-BAS02-1040	Submittal for Slabs Conc. Dim. & RFT DWGs (B04) (Bas 02)	-124	18	24-Jun-26	15-Jul-26
Basement01		-116	21	13-Jul-26	06-Aug-26
F-SUB-B04-BAS01-1030	Submittal for Beams Conc. Dim. & RFT DWGs (B04) (Bas 01)	-116	18	13-Jul-26	03-Aug-26
F-SUB-B04-BAS01-1040	Submittal for Slabs Conc. Dim. & RFT DWGs (B04) (Bas 01)	-116	18	16-Jul-26	06-Aug-26
Affected-Activities-Approval		-116	70	23-May-26	18-Aug-26
B01		-97	31	23-May-26	02-Jul-26
Basement02		-113	13	23-May-26	10-Jun-26
F-APP-B01-BAS02-1030	Approval for Beams Conc. Dim. & RFT DWGs (B01) (Bas 02)	-110	10	23-May-26	07-Jun-26
F-APP-B01-BAS02-1040	Approval for Slabs Conc. Dim. & RFT DWGs (B01) (Bas 02)	-113	10	26-May-26	10-Jun-26
Basement01		-97	13	17-Jun-26	02-Jul-26
F-APP-B01-BAS01-1030	Approval for Beams Conc. Dim. & RFT DWGs (B01) (Bas 01)	-94	10	17-Jun-26	28-Jun-26
F-APP-B01-BAS01-1040	Approval for Slabs Conc. Dim. & RFT DWGs (B01) (Bas 01)	-97	10	21-Jun-26	02-Jul-26
B02		-93	31	23-May-26	02-Jul-26
Basement02		-107	13	23-May-26	10-Jun-26

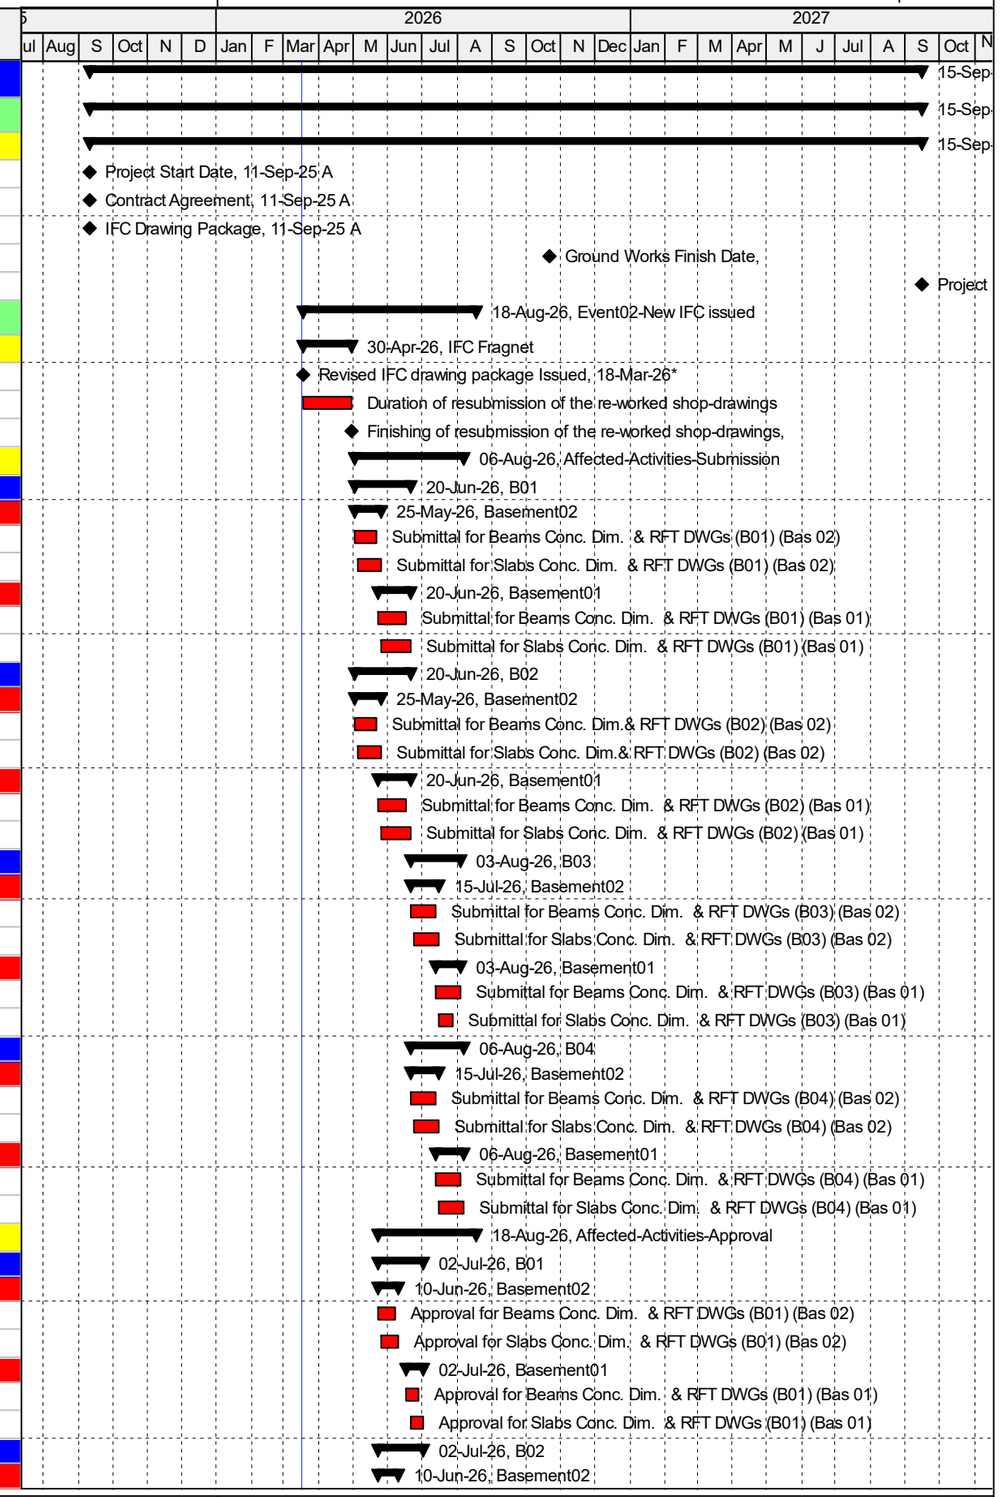

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: wbs.

© Oracle Corporation

Activity ID	Activity Name	Total Float	Original Duration	Start	Finish
F-APP-B02-BAS02-1020	Approval for Beams Conc. Dim. & RFT DWGs (B02) (Bas 02)	-104	10	23-May-26	07-Jun-26
F-APP-B02-BAS02-1030	Approval for Slabs Conc. Dim. & RFT DWGs (B02) (Bas 02)	-107	10	26-May-26	10-Jun-26
Basement01		-93	13	17-Jun-26	02-Jul-26
F-APP-B02-BAS01-1020	Approval for Beams Conc. Dim. & RFT DWGs (B02) (Bas 01)	-90	10	17-Jun-26	28-Jun-26
F-APP-B02-BAS01-1030	Approval for Slabs Conc. Dim. & RFT DWGs (B02) (Bas 01)	-93	10	21-Jun-26	02-Jul-26
B03		-116	28	13-Jul-26	15-Aug-26
Basement02		-132	13	13-Jul-26	28-Jul-26
F-APP-B03-BAS02-1020	Approval for Beams Conc. Dim. & RFT DWGs (B03) (Bas 02)	-129	10	13-Jul-26	25-Jul-26
F-APP-B03-BAS02-1030	Approval for Slabs Conc. Dim. & RFT DWGs (B03) (Bas 02)	-132	10	16-Jul-26	28-Jul-26
Basement01		-116	13	01-Aug-26	15-Aug-26
F-APP-B03-BAS01-1030	Approval for Slabs Conc. Dim. & RFT DWGs (B03) (Bas 01)	-113	10	01-Aug-26	11-Aug-26
F-APP-B03-BAS01-1020	Approval for Beams Conc. Dim. & RFT DWGs (B03) (Bas 01)	-116	10	04-Aug-26	15-Aug-26
B04		-116	31	13-Jul-26	18-Aug-26
Basement02		-124	13	13-Jul-26	28-Jul-26
F-APP-B04-BAS02-1030	Approval for Beams Conc. Dim. & RFT DWGs (B04) (Bas 02)	-121	10	13-Jul-26	25-Jul-26
F-APP-B04-BAS02-1040	Approval for Slabs Conc. Dim. & RFT DWGs (B04) (Bas 02)	-124	10	16-Jul-26	28-Jul-26
Basement01		-116	13	04-Aug-26	18-Aug-26
F-APP-B04-BAS01-1030	Approval for Beams Conc. Dim. & RFT DWGs (B04) (Bas 01)	-113	10	04-Aug-26	15-Aug-26
F-APP-B04-BAS01-1040	Approval for Slabs Conc. Dim. & RFT DWGs (B04) (Bas 01)	-116	10	08-Aug-26	18-Aug-26

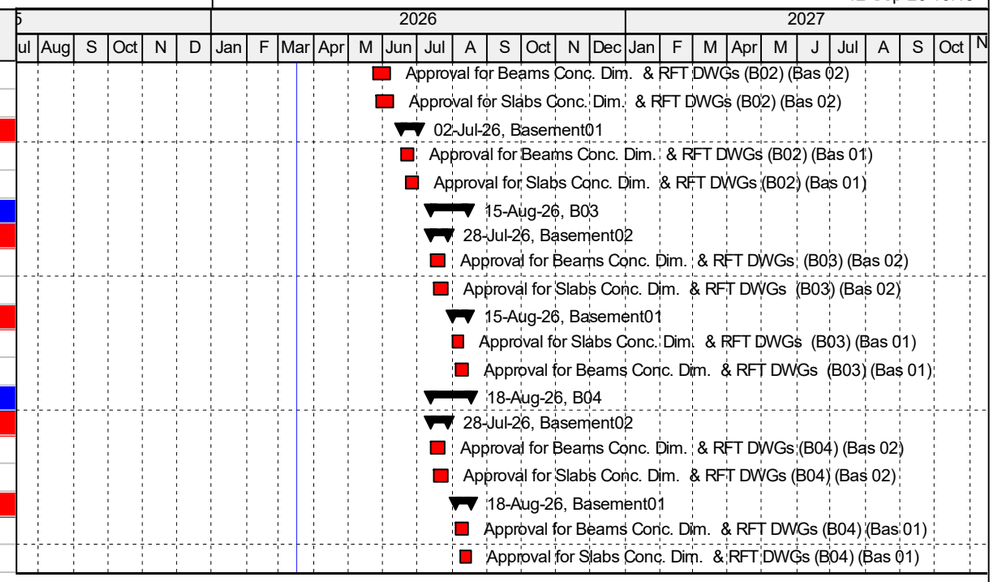

Actual Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: wbs.

© Oracle Corporation
